



# Measure E Bond Program COLUMBIA COLLEGE CAMPUS CONSTRUCTION UPDATE



## UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION *Week of August 19, 2013*

### MJC NURSING COHORT - REDBUD

**Work this week:** The GC is scheduled to work on punch list items and change order work. AV system will continue being installed.

- Access:** Limited access through drive isle north of building.  
**Noise:** Moderate noise could occur occasionally.  
**Parking:** Parking impact due to contractor's parking along drive isle.  
**Dust:** Low Impact.  
**Odors:** Low Impact.  
**Utilities:** No impact to utilities is anticipated.



## Secondary Data Center

**Work this week:** This week's work includes completion of mechanical, electrical and plumbing systems inside walls and ceilings. Outside the building, the elevator landing and machine room slabs will be poured. MEP trades will continue installing underground utilities and the roofer will continue upgrading the roof.



**Access:** Caution is advised at tennis courts and student trail south of building.  
**Noise:** Moderate noise could occur occasionally due to site related activities.  
**Parking:** Moderate impact to parking at tennis courts due to contractor's staging of construction materials.  
**Dust:** Moderate impact due to site related construction activities.  
**Odors:** Low Impact  
**Utilities:** No impact to utilities is anticipated.



## Roadways Phase I

**Work this week:** This week the GC work on correcting punch list items and finish striping at new areas that require it. Also, fencing will be installed along 3 areas of walkway between Manzanita and Tamarack buildings.

**Access:** limited access to Oak Pavilion parking lot and no access to Symons Field Rd.  
**Noise:** Moderate noise.  
**Parking:** No Parking at Oak Pavilion parking lot.  
**Dust:** Moderate impact due to site related construction activities.  
**Odors:** Low Impact.  
**Utilities:** No impact to utilities is anticipated.

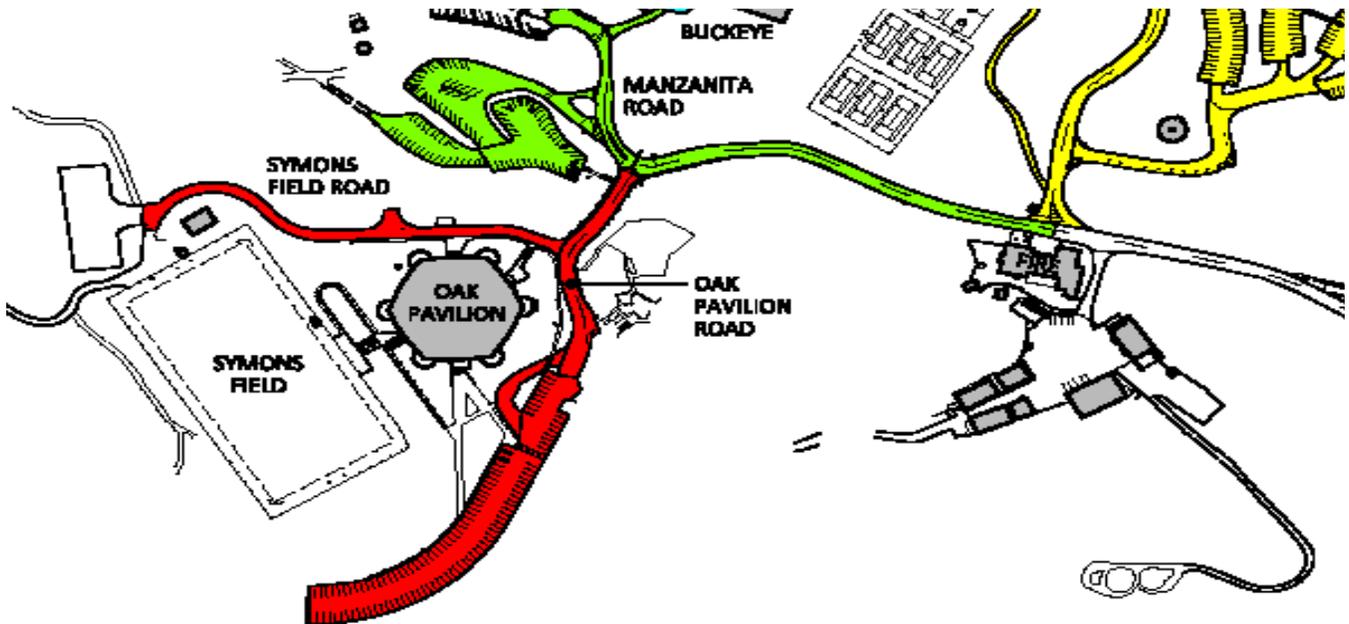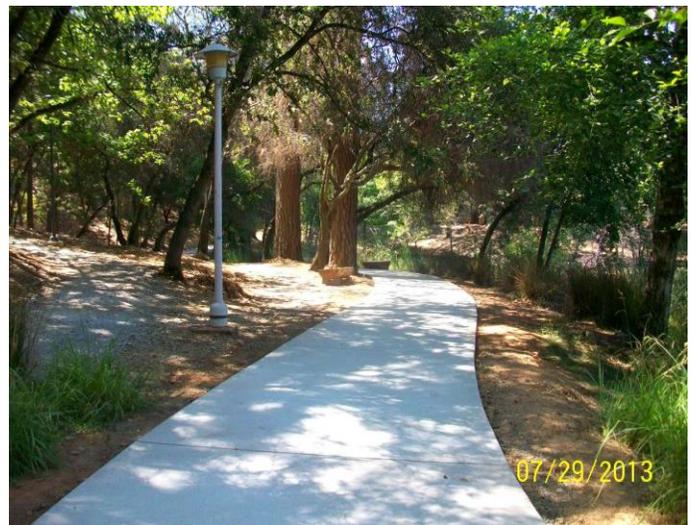

## Sequoia Building Modernization

**Work this week:** This week's work will include demolition of components of existing mechanical, electrical and plumbing systems along with architectural elements such as interior wall veneers, window treatments, flooring and ceiling materials. Interior wall framing will get started as well.

**Access:** No impact anticipated.

**Noise:** Moderate noise could occur occasionally due to demolition activities.

**Parking:** No parking along section of north drive isle adjacent to the construction site.

**Dust:** Moderate noise could occur occasionally due to demolition activities.

**Odors:** Low Impact

**Utilities:** No impact to utilities is anticipated.

