



Measure E Bond Program COLUMBIA COLLEGE CAMPUS CONSTRUCTION UPDATE



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

Week of July 14, 2014

Manzanita Building Modernization

Work this week: Electrical, mechanical and fire sprinkler installation will continue for the upcoming week. The potholing work on Manzanita Road will also continue through the week. We have scheduled to install fascia and glulam caps for this week as well.


Access:	Caution is advised when entering the site due to tripping hazards.
Noise:	Moderate to extreme noise could occur occasionally due to site related activities.
Parking:	Low impact.
Dust:	Moderate impact due to site related construction activities.
Odors:	Low Impact
Utilities:	None anticipated.



Roadways Phase II

Work this week: Asphalt in front of student housing has been demoed. The handicap walkway is scheduled to be done next week. On the 16th, 17th & 18th we will begin to pave roads.

Access: Caution is advised when entering the site due to traffic detours & worker/equipment exposure.
Noise: Moderate to extreme noise could occur occasionally due to site related activities.
Parking: High impact; road closures & detours have been implemented. Bulletins of these closures/detours have been delivered to the District for distribution.
Dust: Moderate impact due to site related construction activities.
Odors: Low Impact
Utilities: None anticipated.

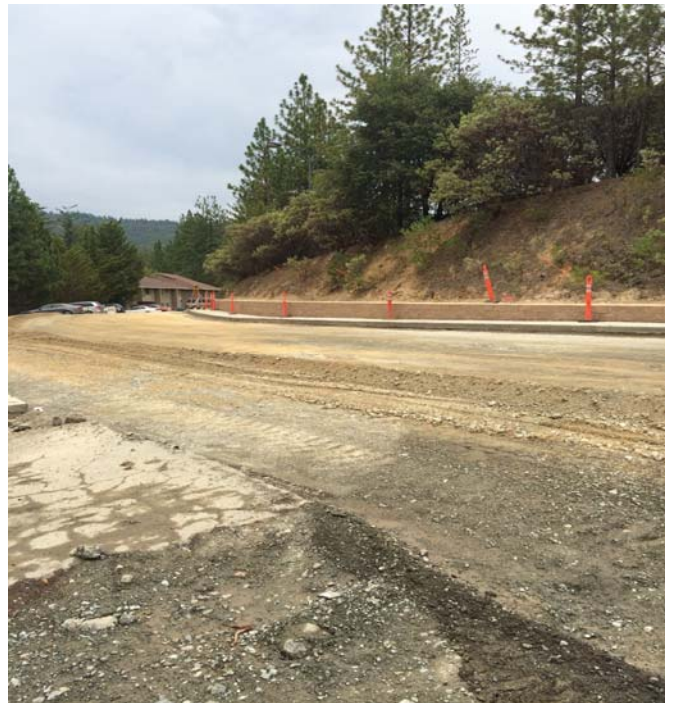

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at
11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email rmartin@kitchell.com

