

Measure E Bond Program COLUMBIA COLLEGE CAMPUS

CONSTRUCTION UPDATE



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

Week of February 9, 2015

Manzanita Building Modernization

Work this week: For the second week of February we will wrap up texturing of walls inside the building. Painting has commenced in some sections of the building & will run through the week. The entry archway saw some paint application the prior week & it should be complete this week. Electrical & mechanical work will each continue. We will begin to install T-bar grid near the end of the week along with light fixture installation.


Access: Caution is advised when entering the site due to tripping hazards.

Noise: Moderate to extreme noise could occur occasionally due to site related activities.

Parking: Low impact.

Dust: Moderate impact due to site related construction activities.

Odors: Low Impact Utilities: None anticipated.

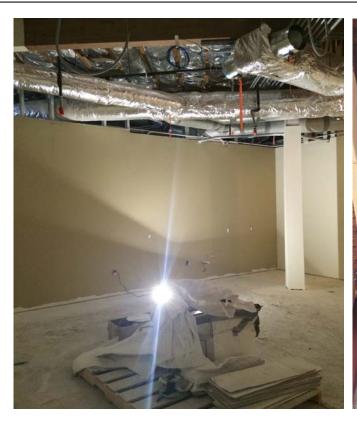



If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email rmartin@kitchell.com

