



Measure E Bond Program COLUMBIA COLLEGE CAMPUS *CONSTRUCTION UPDATE*



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

Week of February 23, 2015

Manzanita Building Modernization

Work this week: Painting is about 90% complete & should wrap up this week. During our last week of February we will continue installing T-bar grid for the building and that will also come to a close. For the first couple of days we will complete tile installation in the rest rooms. New items for this week include installation of trim & siding along with doors & hardware. Electrical & mechanical work continues to progress.


Access:	Caution is advised when entering the site due to tripping hazards.
Noise:	Moderate to extreme noise could occur occasionally due to site related activities.
Parking:	Low impact.
Dust:	Moderate impact due to site related construction activities.
Odors:	Low Impact
Utilities:	None anticipated.



Roadways Madrone Road

Work this week: Construction on the hillside has made a great leap. The holes for the hillside have all been drilled. We were able to install rebar & the wire mesh along the hill to wrap up the week. The drainage pipe has also been installed & covered with slurry. For the coming week we will see no construction on Monday due to the coming rain however for the rest of the week we will see shotcrete application onto the hillside.

Access: Caution is advised when entering the site due to construction all along the hillside.
Noise: Moderate to extreme noise could occur occasionally due to site related activities.
Parking: Low impact.
Dust: Moderate impact due to site related construction activities.
Odors: Low Impact
Utilities: None anticipated.

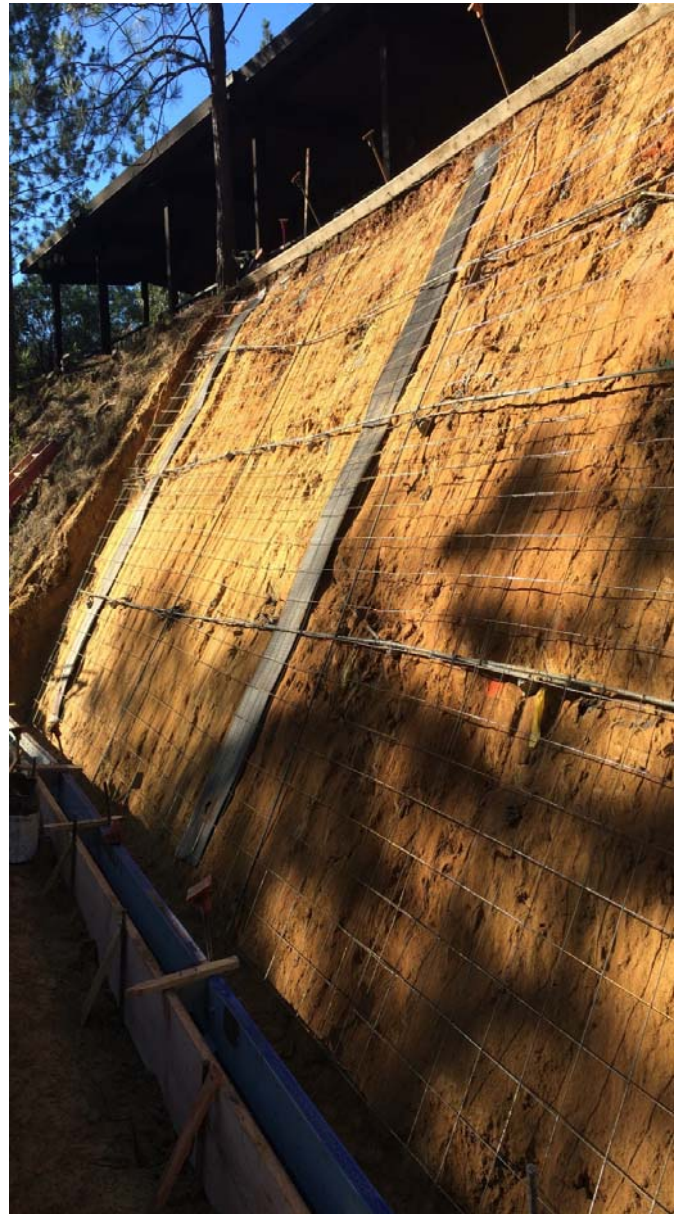

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email rmartin@kitchell.com

