



## Measure E Bond Program COLUMBIA COLLEGE CAMPUS CONSTRUCTION UPDATE



### UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

*Week of April 6, 2015*

#### Manzanita Building Modernization

**Work this week:** This week electrical work will keep rolling as we will be installing conduit & wiring at the bollards. Through the week we will also be installing Data & CCTV cable. For the first two days we will see our marker boards put in. Installation of fabric wrapped panels & the artwork hanging system will follow. Outside of the building we will have site work for pavers occurring.


<b>Access:</b>	Caution is advised when entering the site due to tripping hazards.
<b>Noise:</b>	Moderate to extreme noise could occur occasionally due to site related activities.
<b>Parking:</b>	Low impact.
<b>Dust:</b>	Moderate impact due to site related construction activities.
<b>Odors:</b>	Low Impact
<b>Utilities:</b>	None anticipated.



## Roadways Madrone Road

**Work this week:** Madrone road is now paved & speed bumps have been installed. We will have no crews on site as the road will be left alone for a couple of weeks before striping can begin.

**Access:** Madrone Road is open for pedestrian & vehicular traffic.  
**Noise:** No impact anticipated.  
**Parking:** No impact anticipated.  
**Dust:** No impact anticipated.  
**Odors:** No impact anticipated.  
**Utilities:** None anticipated.

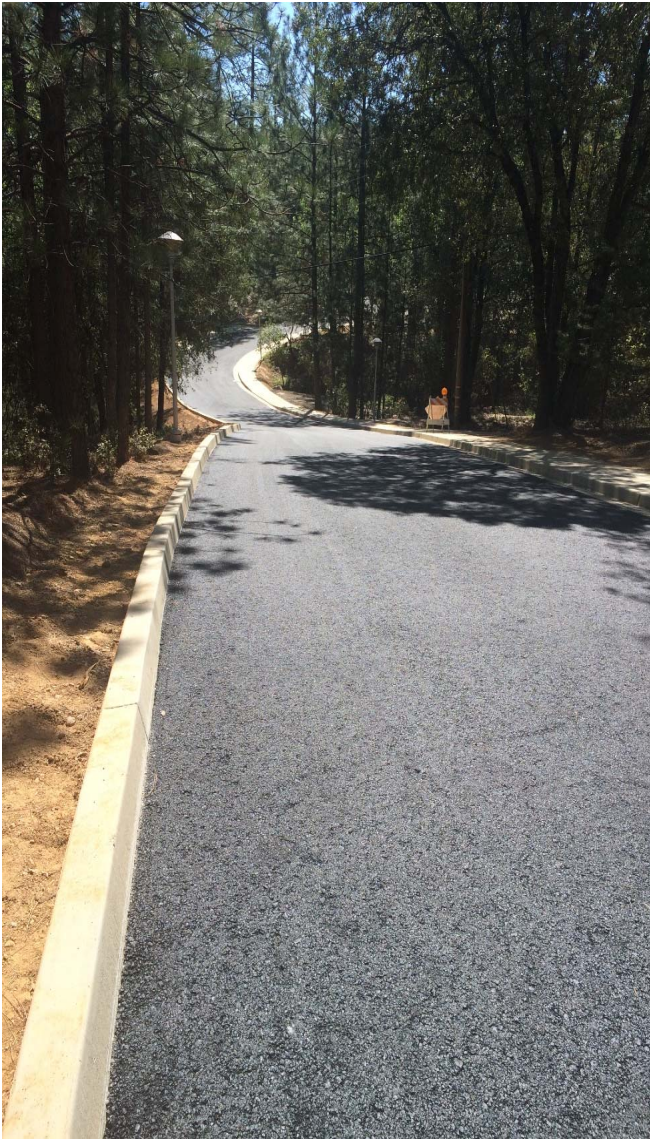

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email [rmartin@kitchell.com](mailto:rmartin@kitchell.com)

