



Measure E Bond Program COLUMBIA COLLEGE CAMPUS CONSTRUCTION UPDATE



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION *Week of May 11, 2015*

Manzanita Building Modernization

Work this week: Starting the month of May we will be wrapping up construction activity. For this week exterior paint application will continue. Glass marker boards are now up & we are going to continue installing redwood trim around them. Tack board is due to be installed this week. Flooring is complete & we are now installing vinyl baseboard throughout the building which will be complete at the end of the week. Minor electrical work continues with the calibration of lighting to take place. Miscellaneous work will occur throughout the coming days along with extensive cleaning.


Access:	Caution is advised when entering the site due to tripping hazards.
Noise:	Moderate to extreme noise could occur occasionally due to site related activities.
Parking:	Low impact.
Dust:	Moderate impact due to site related construction activities.
Odors:	Low Impact
Utilities:	None anticipated.



Roadways Phase III

Work this week: Our newest roads project has kicked off! Pulverizing of the roads is underway from child development down to Willow. All next week the contractor will be working on grading this area.

Access: Caution is advised when entering the site due to tripping hazards & construction related activities.
Noise: Moderate to extreme noise could occur occasionally due to site related activities.
Parking: Moderate impact as staff parking has been relocated to the Oak Pavilion Lot.
Dust: Moderate impact due to site related construction activities.
Odors: Low Impact.
Utilities: None anticipated.

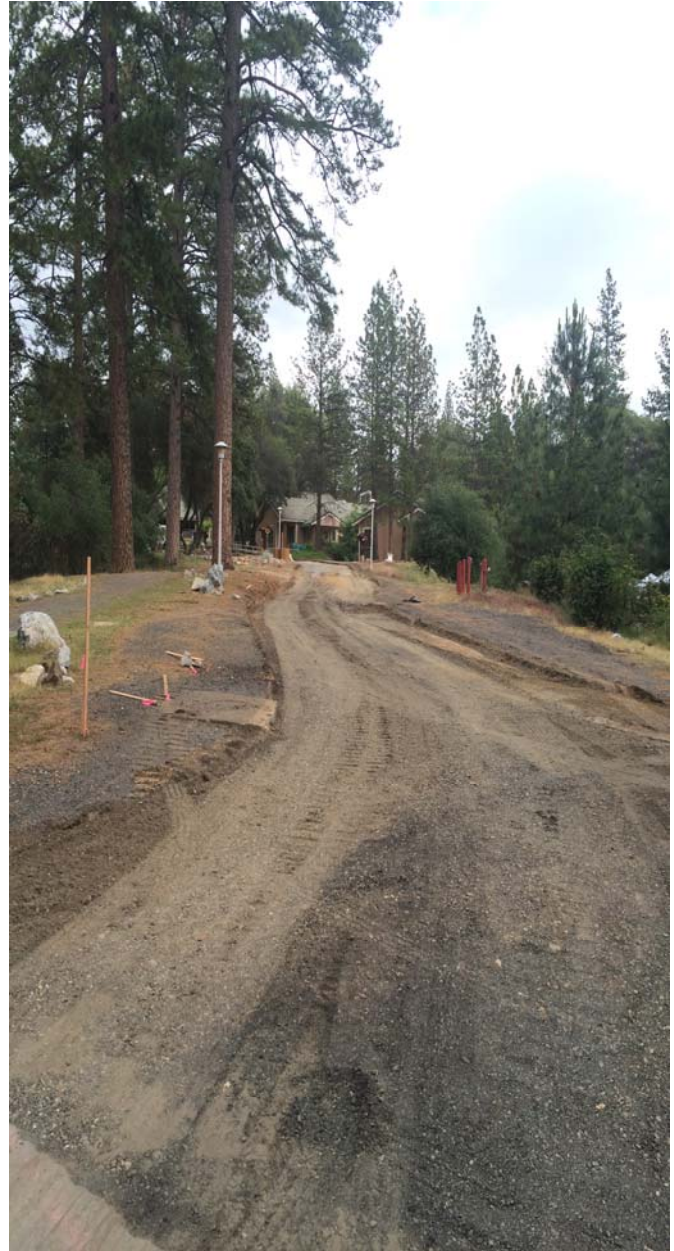

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email rmartin@kitchell.com

