



Measure E Bond Program COLUMBIA COLLEGE CAMPUS *CONSTRUCTION UPDATE*



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION *Week of April 13, 2015*

Manzanita Building Modernization

Work this week: Things will be moving along rather quickly these upcoming weeks as we are getting closer & closer to project completion. For outside work will be installing pavers throughout the week as well as pouring our slab for the ADA parking near the loading dock. We will begin to start paint for the exterior of the building. Floor prep for carpet & flooring install has begun and will also run through the week. Electrical work will be occurring all week. Towards the end of the week we will install the artwork hanging system & partitions finishing up with fire alarm testing on Friday.


Access:	Caution is advised when entering the site due to tripping hazards.
Noise:	Moderate to extreme noise could occur occasionally due to site related activities.
Parking:	Low impact.
Dust:	Moderate impact due to site related construction activities.
Odors:	Low Impact
Utilities:	None anticipated.



Roadways Madrone Road

Work this week: We will have crews on site that will be doing striping work on the road. They will also be installing signage and these work activities will run through the week.

Access: Caution is advised when entering the site due to tripping hazards & construction related activities.
Noise: Moderate impact due to construction related activities.
Parking: Low impact.
Dust: Moderate impact.
Odors: Moderate impact.
Utilities: None anticipated.

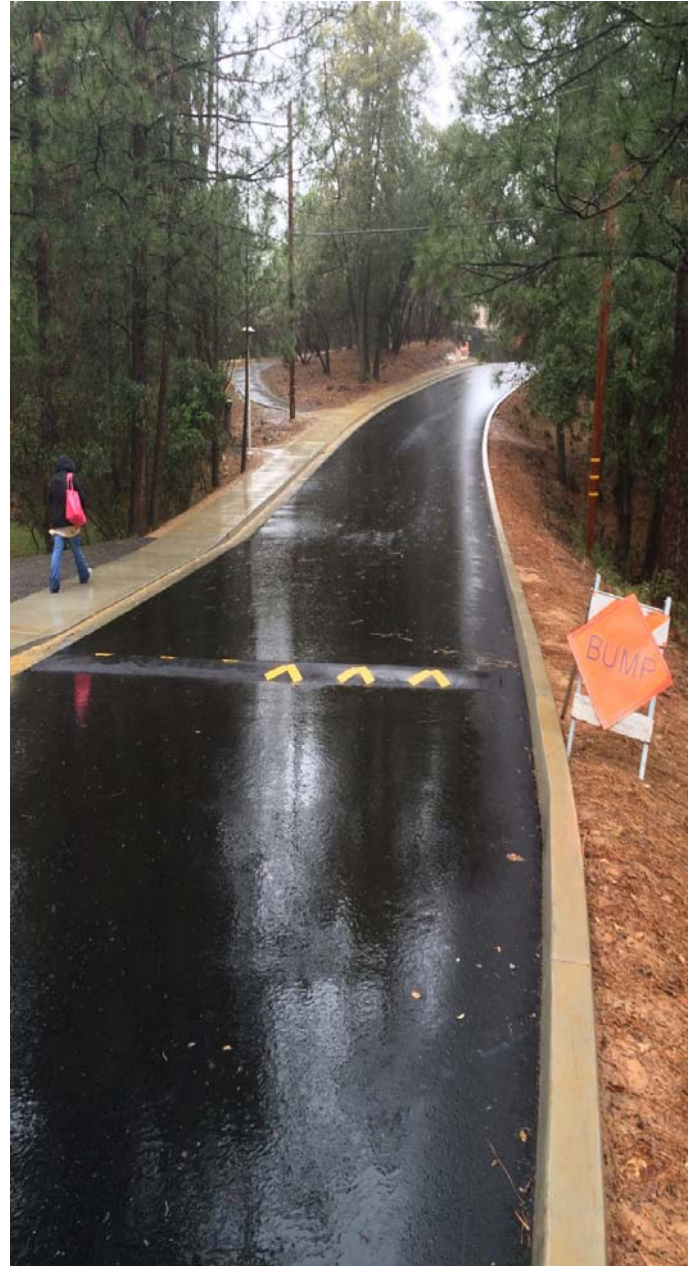

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email rmartin@kitchell.com

