



## Measure E Bond Program COLUMBIA COLLEGE CAMPUS *CONSTRUCTION UPDATE*




### UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION *Week of June 15, 2015*


#### Manzanita Building Modernization

**Work this week:** This coming week we will be moving in the final set of users into the building. By the end of the week we will have full occupancy. We will continue to help the users adjust to their new spaces, troubleshoot any issues that arise as well as answer any questions they have. We have one electrician on site doing some minor electrical work. Painters are also on site finishing up some detailing on the exterior of the building.

<b>Access:</b>	Caution is advised when entering the site due to tripping hazards.
<b>Noise:</b>	Low impact as the construction activities left cause minimal sound disturbance.
<b>Parking:</b>	Low impact.
<b>Dust:</b>	Low impact.
<b>Odors:</b>	Low Impact
<b>Utilities:</b>	None anticipated.

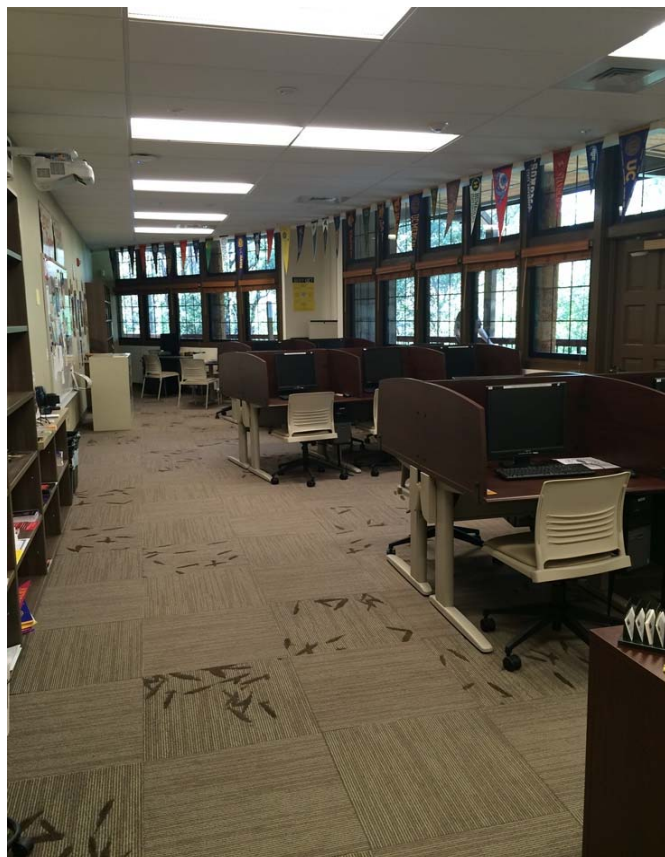

**Assessment & Career Transfer Room**

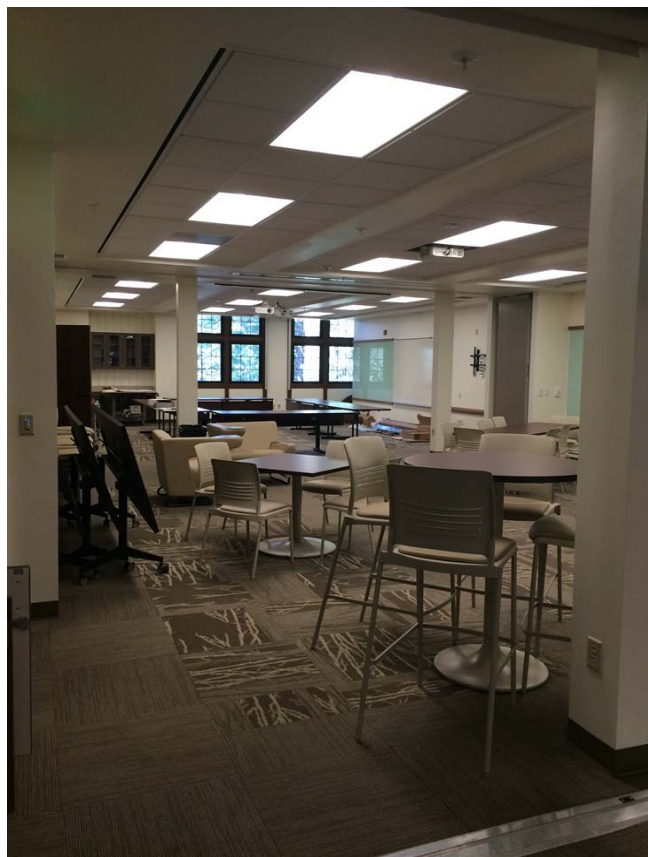

**Multi-purpose Room**



## Roadways Phase III

**Work this week:** Sidewalks, curbs & gutters have been set & poured on Manzanita Road. The aggregate base is set in the staff parking lot and this coming week we will begin to place the AB on Manzanita Road.

**Access:** Caution is advised when entering the site due to tripping hazards & construction related activities.  
**Noise:** Moderate to extreme noise could occur occasionally due to site related activities.  
**Parking:** Moderate impact as staff parking has been relocated to the Oak Pavilion Lot.  
**Dust:** Moderate impact due to site related construction activities.  
**Odors:** Low Impact.  
**Utilities:** None anticipated.



**Sidewalk (Front of staff parking lot)**



**Staff lot (Finished AB)**

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email [rmartin@kitchell.com](mailto:rmartin@kitchell.com)

