

Measure E Bond Program COLUMBIA COLLEGE CAMPUS

CONSTRUCTION UPDATE



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

Week of June 22, 2015

Manzanita Building Modernization

Work this week: The Manzanita building is now fully occupied with all the user groups. For this week we will continue to assist users with any issues they have or that may arise. Minor electrical work continues along with paint touch ups on the exterior of the building. Our elevator work is scheduled to begin this week and will be completed in approximately two weeks.

Access: Caution is advised when entering the site due to tripping hazards.

Noise: Low impact as the construction activities left cause minimal sound disturbance.

Parking: Low impact.

Dust: Low impact.

Odors: Low Impact

Utilities: None anticipated.





Manzanita Conference Room

Flat screen TV in Rotunda

Roadways Phase III


Work this week: Now that the staff parking lot & Manzanita road have been paved we will move work towards Columbia College Drive. This week we will grade curb & gutter and begin to form the sidewalk along the road towards the end of the week.

Access: Caution is advised when entering the site due to tripping hazards & construction related activities.

Noise: Moderate to extreme noise could occur occasionally due to site related activities. **Parking:** Moderate impact as staff parking has been relocated to the Oak Pavilion Lot.

Dust: Moderate impact due to site related construction activities.

Odors: Low Impact.
Utilities: None anticipated.

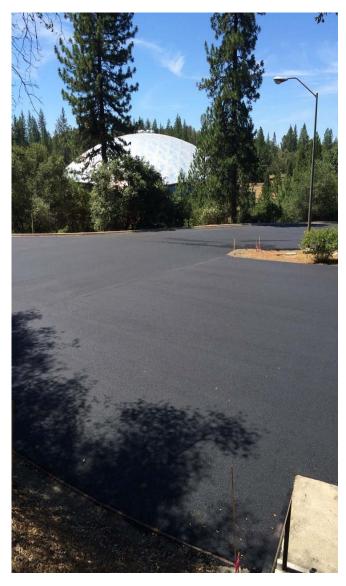



Asphalt (Staff parking lot)

Asphalt (Manzanita Road)

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email rmartin@kitchell.com

