

## Measure E Bond Program Phase I Projects

### PROGRAM PROGRESS

Campus-wide CEQA (CA Environmental Quality Act) compliance documentation is in process.

### DESIGN PROGRESS

**Public Safety Center:** Abatement bids were received at the end of January. DSA has completed review of construction documents. Bidding is anticipated for February 2008.

**Madrone Building:** DSA has completed first plan check review of the construction documents. Final review for approval is scheduled for February 2008. Bidding is scheduled for March 2008 with construction anticipated to start in April 2008.

**Science & Natural Resources Center:** Project committee continues to meet with the design team on schematic design phase.

**Child Development:** Construction documents were submitted to DSA for review this past December. DSA final approval is scheduled to be completed by April 2008. Project Team anticipates bidding in June 2008.

**Calaveras (Land Acquisition):** An appraisal report is in process for Board review.


**Oakdale (Land Acquisition):** The college and district are in the process of reviewing possible sites for future location.

**Scheduled Maintenance – Re-Roof Madrone (Welding) & (Auto):** Construction documents are being reviewed by DSA. Bidding is anticipated for May 2008 with construction in June 2008.

### CONSTRUCTION PROGRESS

**Buckeye Sewer Pump Replacement:** Project was bid and construction was completed in December without causing disruptions to the facility.

## Science & Natural Resource Center – Schematic Design Preliminary 1<sup>st</sup> Floor Plan

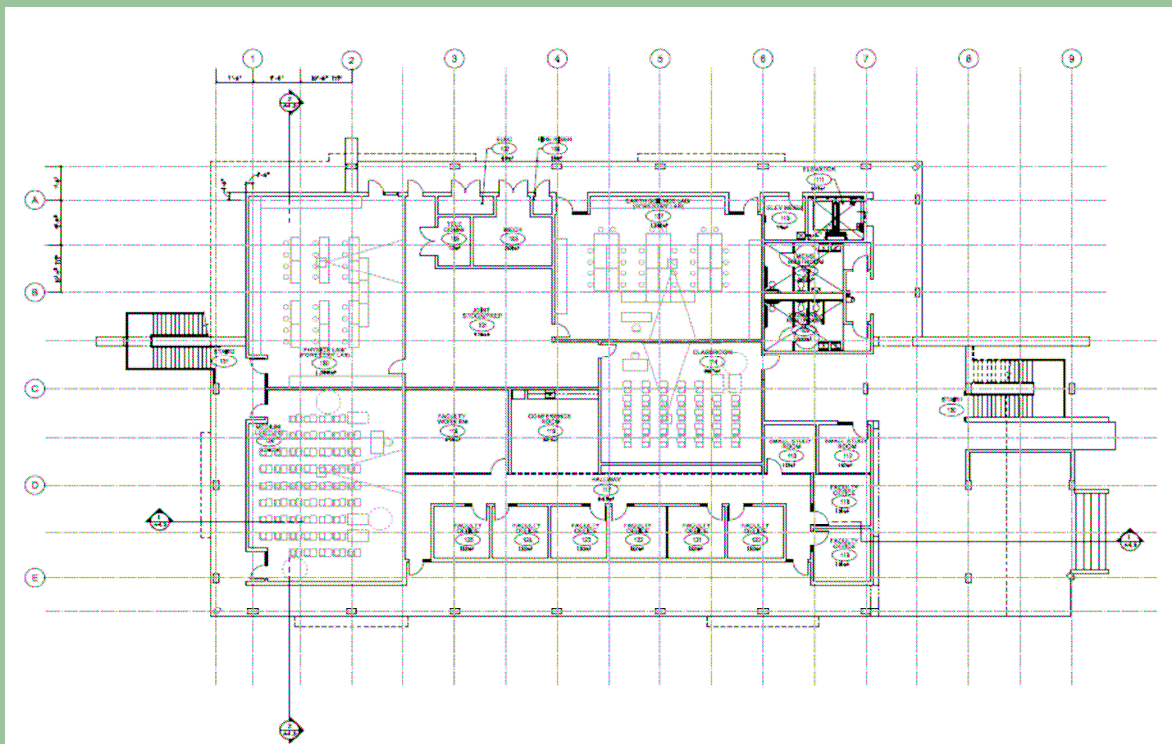

If you have any questions or concerns about ongoing construction activities or would like to get additional information about ongoing design projects, please contact Kitchell, CEM at 575-6991.
