

June 2008

Measure E Bond Program Phase I Projects

PROGRAM PROGRESS

Campus-wide CEQA (CA Environmental Quality Act) compliance documentation was completed in May. The Initial Study shows that the Phase I projects should have no significant impacts on the site.

DESIGN PROGRESS

Madrone Building: Bidding phase is expected to start June 2nd and construction is anticipated to start mid-July.

Science & Natural Resources Center: The Design Development Phase is underway with laboratory equipment, mechanical, electrical and civil design meetings scheduled for this month.

Child Development Center: DSA review is nearing completion. Project is anticipated to bid mid-June and construction is expected to start late July.

Calaveras Educational Site: YCCD Board of Trustees has authorized the District to begin negotiations for the purchase of property located in Angels Camp.

Oakdale Educational Site: The College and the Yosemite Community College District continue to review possible sites for a future location.

SCHEDULED MAINTENANCE PROGRESS

Re-Roof Madrone (Auto and Welding) and Buckeye:

The bidding phase has been completed. Construction is expected to start mid-June and its anticipated completion date is mid-August.

CONSTRUCTION PROGRESS


Re-Roofing Project for Madrone and Buckeye buildings:

Construction is expected to start mid-June with completion anticipated by mid-August.

Public Safety center: Construction is underway and it is anticipated to be complete by May 2009.



**A ground breaking ceremony
for the Public Safety Project
has been scheduled for June 16th.**

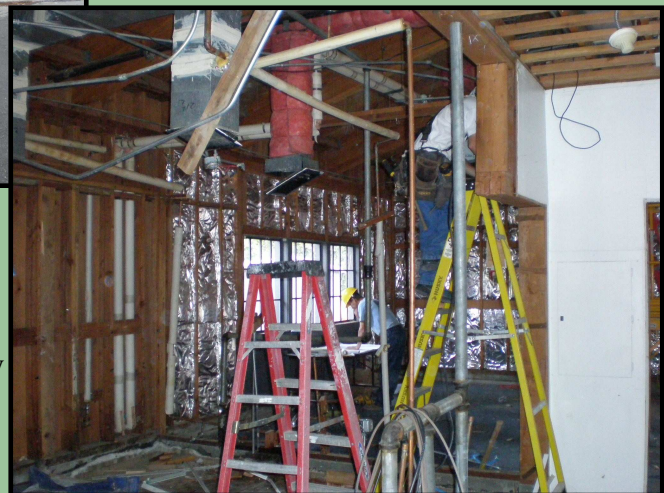

Public Safety Project

Construction began in late May and completion of this project is anticipated by May of 2009.
