



Measure E Bond Program

MJC Auditorium Alterations/Additions

CONSTRUCTION UPDATE

Issue No. 92

AUGUST 29, 2008

1. Work performed during week of 8/25/08:


- a. Continued working on AV punchlist.
- b. Continued installing additional AV equipment.
- c. Continued working on miscellaneous punchlist items.
- d. Issued production lighting and rigging system's punchlist.

2. Work anticipated for week of 9/01/08:

- a. Start working of production lighting and rigging system's punchlist.
- b. Continue installing additional AV equipment.
- c. Complete AV punchlist.
- d. Complete miscellaneous punchlist items.



The Main Stage

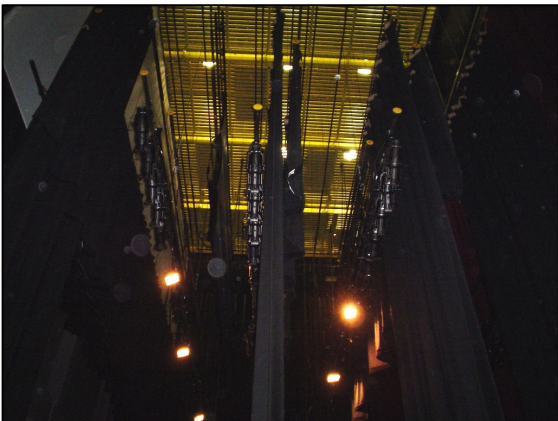

The Main Stage Rigging System

3. Activities that may impact campus operations:

- a. Access: No access issues anticipated.
- b. Noise: None anticipated.
- c. Parking: Parking lot F is now open.
- d. Power outages: None anticipated.
- e. Water off: None anticipated.
- f. Odors: No unusual odors are expected.
- g. Dust: None anticipated.

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at
2201 Blue Gum Ave., Rm #1301, Modesto CA 95358 Tel: 575-6991 Email agourtzelis@kitchell.com

