



Measure E Bond Program MODESTO JUNIOR COLLEGE CAMPUS CONSTRUCTION UPDATE



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION *Week of May 23, 2011*

AGRICULTURE MULTIPURPOSE PAVILION

Work this week: Exterior site work landscape & irrigation, installation of roof panels, insulation, sheet rock and taping, paint, installation of overhead coiling doors, aluminum storefront, casework in classrooms, tile installation in restrooms.

| | |
|-------------------|-----------------|
| Access: | No Impact |
| Noise: | Low to Moderate |
| Parking: | No Impact |
| Utilities: | No |
| Odors: | No |
| Dust: | Minimal |



ALLIED HEALTH BUILDING

Work this week: Frame, sheet-rock, plaster and paint interior walls, install t-bar ceilings and continue interior MEP system rough-ins.

| | |
|-------------------|--|
| Access: | Caution advised at Southeast site entrance |
| Noise: | Moderate |
| Parking: | No impact |
| Utilities: | No |
| Odors: | No |
| Dust: | Minimal |



MECHANICAL PLANT

Work this week: Work on punchlist items.

| | |
|-------------------|-----------|
| Access: | No Impact |
| Noise: | Moderate |
| Parking: | No impact |
| Utilities: | No |
| Odors: | No |
| Dust: | Minimal |





Measure E Bond Program MODESTO JUNIOR COLLEGE CAMPUS CONSTRUCTION UPDATE *continued (page 2 of 4)*

INFRASTRUCTURE INCREMENT I

Work this week: Work on punchlist items.


| | |
|-------------------|-----------|
| Access: | No Impact |
| Noise: | No Impact |
| Parking: | No impact |
| Utilities: | No |
| Odors: | No |
| Dust: | No |



INFRASTRUCTURE INCREMENT II

Work this week: Start grinding E, F and G Streets.

| | |
|-------------------|--|
| Access: | Traffic impact at E, F and G Streets and Sierra Hall Parking Lot entrance. |
| Noise: | Construction equipment. |
| Parking: | No parking at "Trailer Row". |
| Utilities: | No |
| Odors: | No |
| Dust: | Yes. High/Moderate. |

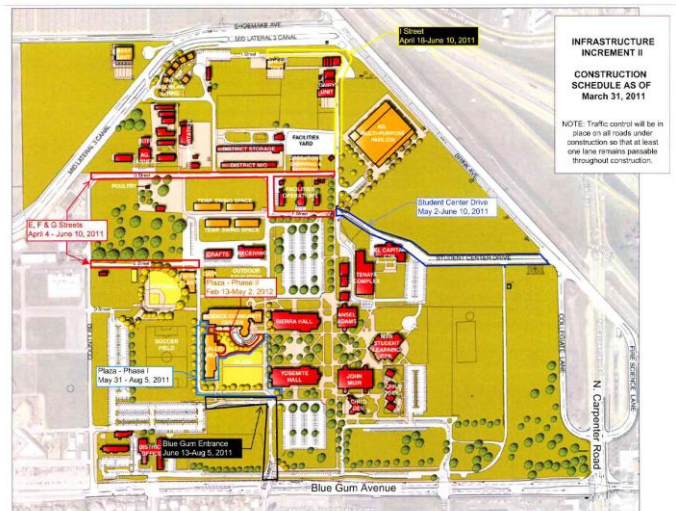

SCIENCE COMMUNITY CENTER

Work this week: Erect structural steel, spread deck, weld. Install formwork/rebar - Observatory, first lift.

| | |
|-------------------|-----------------------|
| Access: | Minor impact |
| Noise: | Moderate impact |
| Parking: | No anticipated impact |
| Utilities: | No anticipated impact |
| Odors: | No anticipated impact |
| Dust: | No anticipated impact |





Measure E Bond Program MODESTO JUNIOR COLLEGE CAMPUS CONSTRUCTION UPDATE *Continued (page 3 of 4)*

NEW STUDENT SERVICES

Work this week: Continue installing duct work, electrical, and plumbing on first and second floor. Interior framing on second floor and first floor is 90% complete. Continue installation of exterior wall covering and roofing. Contractor started stocking gypsum board.

| | |
|-------------------|----------------------------------|
| Access: | No impact |
| Noise: | Moderate: equipment & deliveries |
| Parking: | No additional impacts |
| Utilities: | None |
| Odors: | Yes, cutting of metal materials |
| Dust: | None |



FOUNDERS HALL RENOVATION

Work this week: Mechanical finish, electrical finish, lighting, ceiling tile installation. Fire alarm installation is in process. Roof work in ongoing.

| | |
|-------------------|---|
| Access: | Ramp between Forum and Founders closed. |
| Noise: | Deliveries |
| Parking: | No additional impacts |
| Utilities: | None |
| Odors: | None |
| Dust: | Minimal |



SOFTBALL FIELD RESTROOM/CONCESSION STAND

Work this week: Roofing and plumbing installation.

| | |
|-------------------|------------|
| Access: | No Impact |
| Noise: | Minimal |
| Parking: | No Impacts |
| Utilities: | None |
| Odors: | None |
| Dust: | Minimal |





Measure E Bond Program MODESTO JUNIOR COLLEGE CAMPUS CONSTRUCTION UPDATE *Continued (page 4 of 4)*

ART BUILDING LIFE SAFETY UPGRADES

Work this week: Contractor started demolition in restrooms mechanical systems and plumbing and started clear and grub for kiln yard.

| | |
|-------------------|---------------------|
| Access: | No Impact |
| Noise: | Concrete Demolition |
| Parking: | No Impacts |
| Utilities: | None |
| Odors: | None |
| Dust: | Minimal |



If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 2201 Blue Gum Ave., Rm #1301, Modesto CA 95358 Tel: 575-6991 Email tmillman@kitchell.com

