



Measure E Bond Program COLUMBIA COLLEGE CAMPUS CONSTRUCTION UPDATE



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

Week of July 29, 2013

MJC NURSING COHORT - REDBUD

Work this week: All trades are scheduled to work on punch list items. Furniture will be delivered and installed. AV system will continue being installed.

- Access:** Limited access through drive isle north of building.
Noise: Moderate noise could occur occasionally.
Parking: Parking impact due to contractor's parking along drive isle.
Dust: Low Impact.
Odors: Low Impact.
Utilities: No impact to utilities is anticipated.



Secondary Data Center

Work this week: This week's work includes continue installation of mechanical, electrical and plumbing systems and framing interior walls. Outside the building, the elevator foundation will be formed up, MEP trades will continue installing underground utilities and the roofer will continue upgrading the roof.

Access: Caution is advised at tennis courts and student trail south of building.
Noise: Moderate noise could occur occasionally due to site related activities.
Parking: Moderate impact to parking at tennis courts due to contractor's staging of construction materials.
Dust: Moderate impact due to site related construction activities.
Odors: Low Impact
Utilities: No impact to utilities is anticipated.



Roadways Phase I

Work this week: This week's activities include fine grading, placing of AB and forming new walkways at Symons Field Road and Ag Pavilion parking lot. Also, the GC will continue working on walkway between Manzanita and Tamarack buildings.

Access: limited access to Oak Pavilion parking lot and no access to Symons Field Rd. No access to walkway between Manzanita and Tamarack buildings starting Monday the 22th – Wednesday the 31st.


Noise: Moderate noise will occur due to demolition activities.

Parking: Limited Parking at Oak Pavilion parking lot.

Dust: Moderate impact due to site related construction activities.

Odors: Low Impact.

Utilities: No impact to utilities is anticipated.

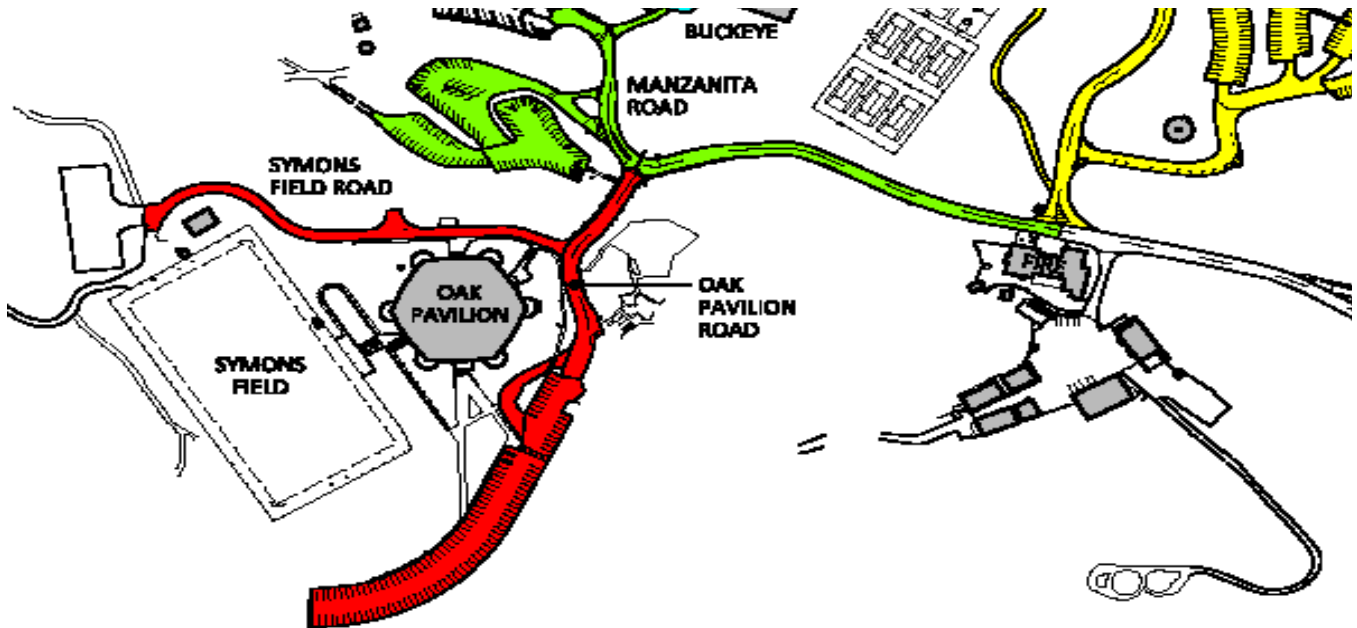

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 2201 Blue Gum Ave., Modesto CA 95358 Tel: 575-6991 Email rmartin@kitchell.com

