

# Measure E Bond Program MODESTO JUNIOR COLLEGE CAMPUS

CONSTRUCTION UPDATE



### UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

Week of April 11, 2011

### AGRICULTURE MULTIPURPOSE PAVILION

**Work this week:** Exterior site work landscape & irrigation, misc. metal stud framing, installation of roof panels, insulation, sheet rock and taping, paint, installation of overhead coiling doors, aluminum storefront installation.

Access: No Impact
Noise: Low to Moderate
Parking: No Impact

Utilities: No Odors: No Dust: Minimal



#### **ALLIED HEALTH BUILDING**

**Work this week:** Frame, sheet-rock, plaster and paint interior walls, install t-bar ceilings and continue interior MEP system rough-ins.

**Access:** Caution advised at Southeast

site entrance

Noise: Moderate
Parking: No impact
Utilities: No

Utilities:NoOdors:NoDust:Minimal



#### **MECHANICAL PLANT**

Work this week: Work on punchlist items.

Access: No Impact
Noise: Moderate
Parking: No impact
Utilities: No

Odors: No
Dust: No
Minimal





## Measure E Bond Program MODESTO JUNIOR COLLEGE CAMPUS

continued (page 2 of 3)

#### INFRASTRUCTURE INCREMENT I

Work this week: Work on punchlist items.

Access: No Impact
Noise: No Impact
Parking: No impact

Utilities: No Odors: No Dust: No



#### INFRASTRUCTURE INCREMENT II

Work this week: Start grinding E, F and G Streets.

**Access:** Traffic impact at E, F and G

Streets and Sierra Hall Parking

Lot entrance.


Noise: Construction equipment.

Parking: No parking at "Trailer Row".

Utilities: No Odors: No

**Dust:** Yes. High/Moderate.

\*Please reference the map attached for additional information.

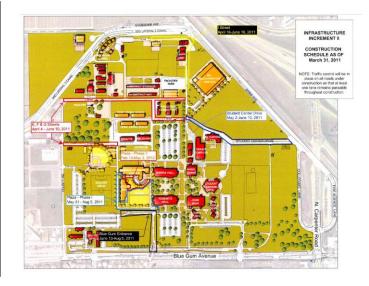

#### **SCIENCE COMMUNITY CENTER**

**Work this week:** Erect structural steel, spread deck, weld. Install formwork/rebar - Observatory, first lift.

Access: Minor impact
Noise: Moderate impact
Parking: No anticipated impact
Utilities: No anticipated impact
Odors: No anticipated impact
No anticipated impact
No anticipated impact





### Measure E Bond Program MODESTO JUNIOR COLLEGE CAMPUS

CONSTRUCTION UPDATE
Continued (page 3 of 3)

#### **NEW STUDENT SERVICES**

**Work this week:** Continue installing duct work, electrical, and plumbing on first and second floor. Continue framing interior walls. Continue installation of exterior wall covering and roofing pending weather.

**Access:** No impact

Noise: Moderate: equipment &

deliveries

**Parking:** No additional impacts

Utilities: None

**Odors:** Yes, cutting of metal materials

**Dust:** None



#### FOUNDERS HALL RENOVATION

**Work this week:** Mechanical work, electrical finish, lighting, plumbing finish, structural steel work, T-Bar installation, and painting. Fire alarm installation in process..

**Access:** Ramp between Forum and Founders closed until May 3<sup>rd</sup>. Student Center Drive one lane shut-down until 4/11/11

**Noise:** Concrete demo & saw cutting

**Parking:** No additional impacts

Utilities: None
Odors: None
Dust: Minimal



### SOFTBALL FIELD RESTROOM/CONCESSION STAND

**Work this week:** Installation of block wall and grouting at the end of the week

Access: No Impact
Noise: Minimal
Parking: No Impacts
Utilities: None
Odors: None
Dust: Minimal



If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 2201 Blue Gum Ave., Rm #1301, Modesto CA 95358 Tel: 575-6991 Email tmillman@kitchell.com



