

**CONSTRUCTION UPDATE** 



### UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

Week of July 4, 2016

#### **DISTRICT OFFICE BUILDING**

**Work this week:** Contractor will continue working on lighting, interior paint, pulling wire, site grading and site concrete.


Access: None

**Noise:** Moderate due to construction equipment.

Parking: None Utilities: None Odors: None

**Dust:** Minor impact.



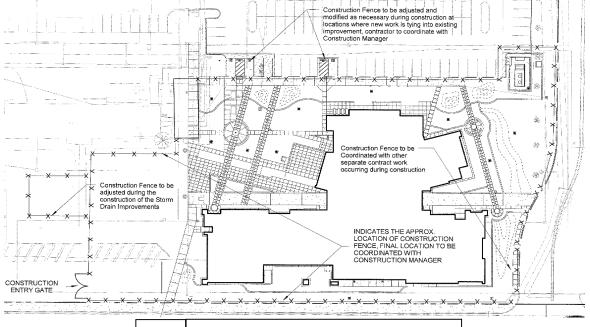



CONSTRUCTION UPDATE Page 2 of 3

#### **WESTERLY ROADS AREAS 3 & 4**

**Work this week:** Paving is complete at Parking Lot 207. On Tuesday paving will occur from F. Street down to E. Street. Grading is taking place on the  $2^{nd}$  half of E. Street headed to the new  $2^{nd}$  Street. Irrigation work will occur at parking lot 207 while electrical continues towards the new  $2^{nd}$  street.

**Access:** Lot 207 is now open for parking.

**Noise:** Extreme noise due to heavy construction equipment.

**Parking:** Gravel lot across E. Street will be closed along with Parking Lot 211.

Utilities: None anticipated.Odors: None anticipated.

**Dust:** Moderate impact due to construction related activities.







CONSTRUCTION UPDATE
Page 3 of 4

#### **WESTERLY ROADS AREAS 5 & 6**

**Work this week:** Work will now continue for our newest road project. Parking lot 211 will be closed for use starting Tuesday as saw cut work will occur from the East side of B Street across from Yosemite Hall down to Parking Lot 209. Demo work will follow in these areas towards the end of the week.

**Access:** Lot 207 is now open for parking.


**Noise:** Extreme noise due to heavy construction equipment.

**Parking:** Gravel lot across E Street will be closed along with Parking Lot 211.

**Utilities:** None anticipated. **Odors:** None anticipated.

**Dust:** Moderate impact due to construction related activities.

### MJC West Campus Westerly Roads Areas 3 & 4 Project

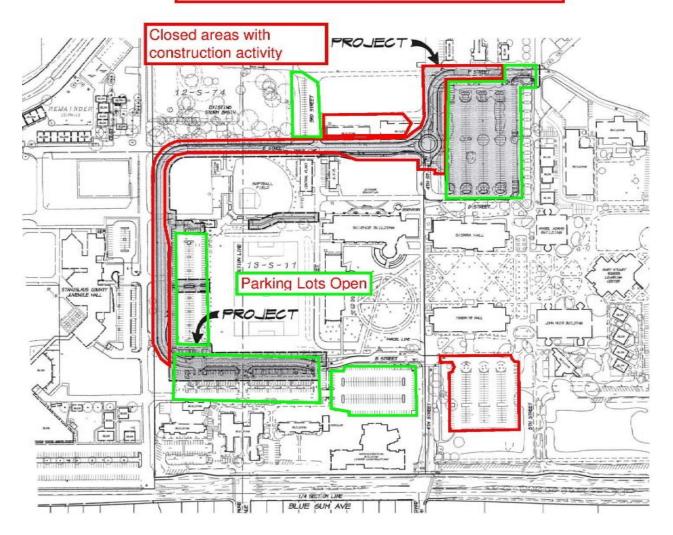



CONSTRUCTION UPDATE Page 4 of 4

#### **SOLAR ARRAY PROJECT**

Work this week: Contractor continues on electrical work installations.

**Access:** None.

**Noise:** Extreme noise due to heavy construction equipment.


**Parking:** Lot 215 will be closed.

**Utilities:** Power shut down at the Central Plant on July 8.

**Odors:** None anticipated.

**Dust:** Moderate impact due to construction related activities.





**Under Construction** 

Available Parking

