



# Measure E Bond Program MODESTO JUNIOR COLLEGE CAMPUS CONSTRUCTION UPDATE




## UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION *Week of April 11, 2016*

### DISTRICT OFFICE BUILDING

**Work this week:** Contractor will be working on mechanical, electrical, and plumbing (MEP) rough-in, wall framing, roofing, exterior lath, and install sheetrock.

**Access:** None  
**Noise:** Moderate due to construction equipment.  
**Parking:** None  
**Utilities:** None  
**Odors:** None  
**Dust:** Minor impact

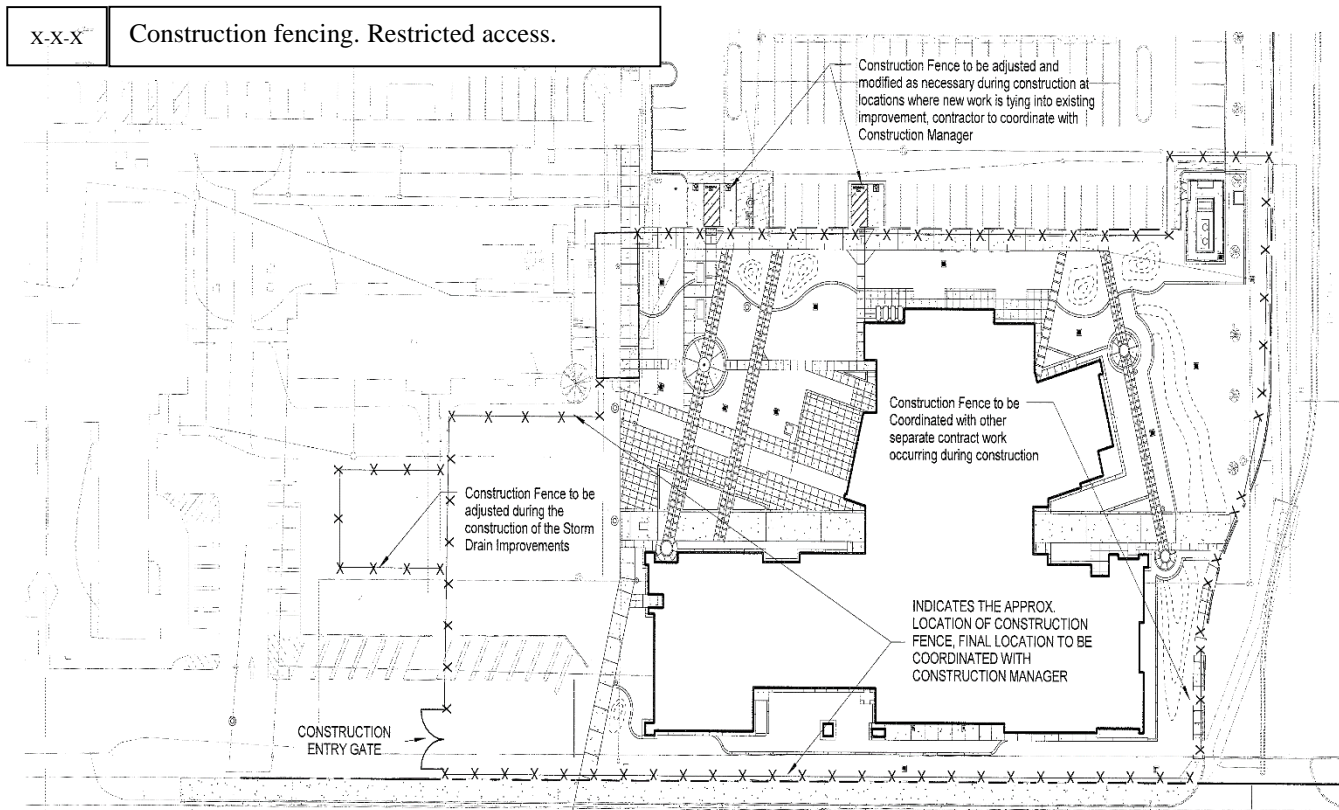



### WESTERLY ROADS AREAS 3 & 4

**Work this week:** The islands at Parking Lot 207 have been completely demoed. The damaged areas of the parking lot that were cut out will get prepped for paving work. Irrigation work will also run through this week. West of the softball field, grading of the dirt areas continues, in preparation for the construction of the new road.

**Access:** Traffic will be redirected to G-Street North of Lot 207.  
**Noise:** Extreme noise due to heavy construction equipment.  
**Parking:** Lot 207 will be closed.  
**Utilities:** None anticipated.  
**Odors:** None anticipated.  
**Dust:** Moderate impact due to construction related activities.

