



Measure E Bond Program COLUMBIA COLLEGE CAMPUS *CONSTRUCTION UPDATE*



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION *Week of March 9, 2015*

Manzanita Building Modernization

Work this week: This week we will wrap up painting of the door & window frames. We will begin to install doors & hardware for the entire week. For the first half of the week we will install partitions & accessories. We will also be installing trim in areas where there are gaps between the drywall & exterior walls.

Access:	Caution is advised when entering the site due to tripping hazards.
Noise:	Moderate to extreme noise could occur occasionally due to site related activities.
Parking:	Low impact.
Dust:	Moderate impact due to site related construction activities.
Odors:	Low Impact
Utilities:	None anticipated.



Roadways Madrone Road

Work this week: The East & West sides of the road have been pulverized & demoed. Those areas were also compacted & subgrade has been set. This week we will be grading & placing curbs & walkways. Concrete crews will be on site at the end of the week.

Access: Caution is advised when entering the site due to construction all along the hillside. One lane traffic will continue as the road demolition & grading will slightly delay traffic flow.



Noise: Moderate to extreme noise could occur occasionally due to site related activities.

Parking: Moderate impact.

Dust: High impact due to site related construction activities.

Odors: Moderate Impact

Utilities: None anticipated.

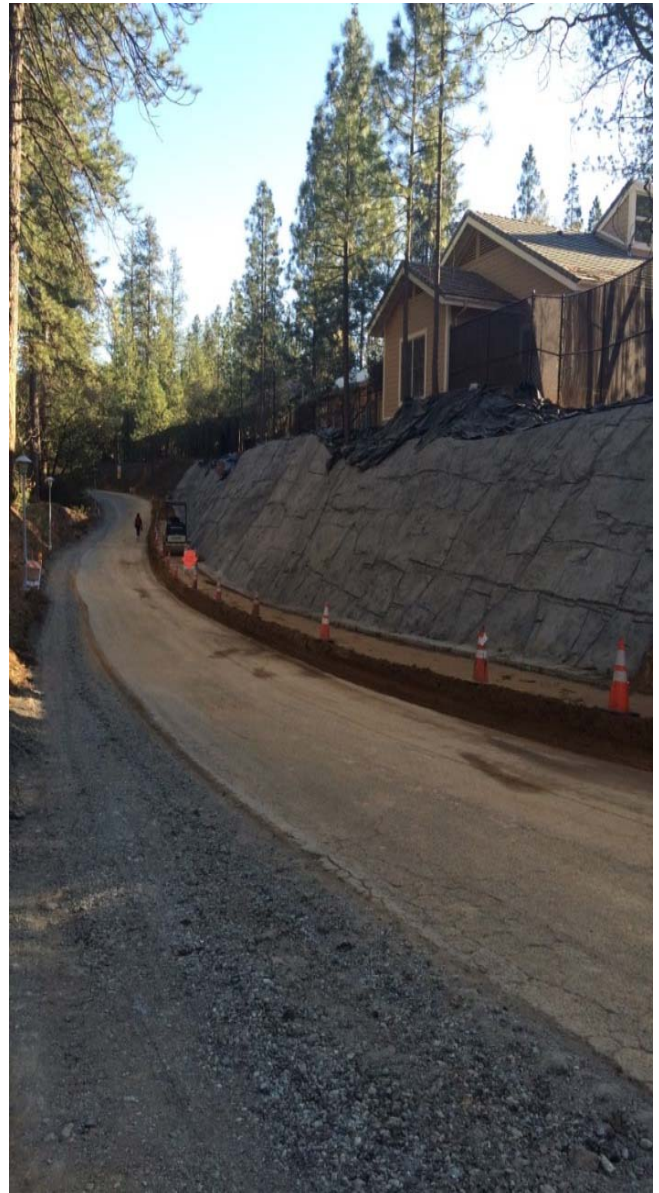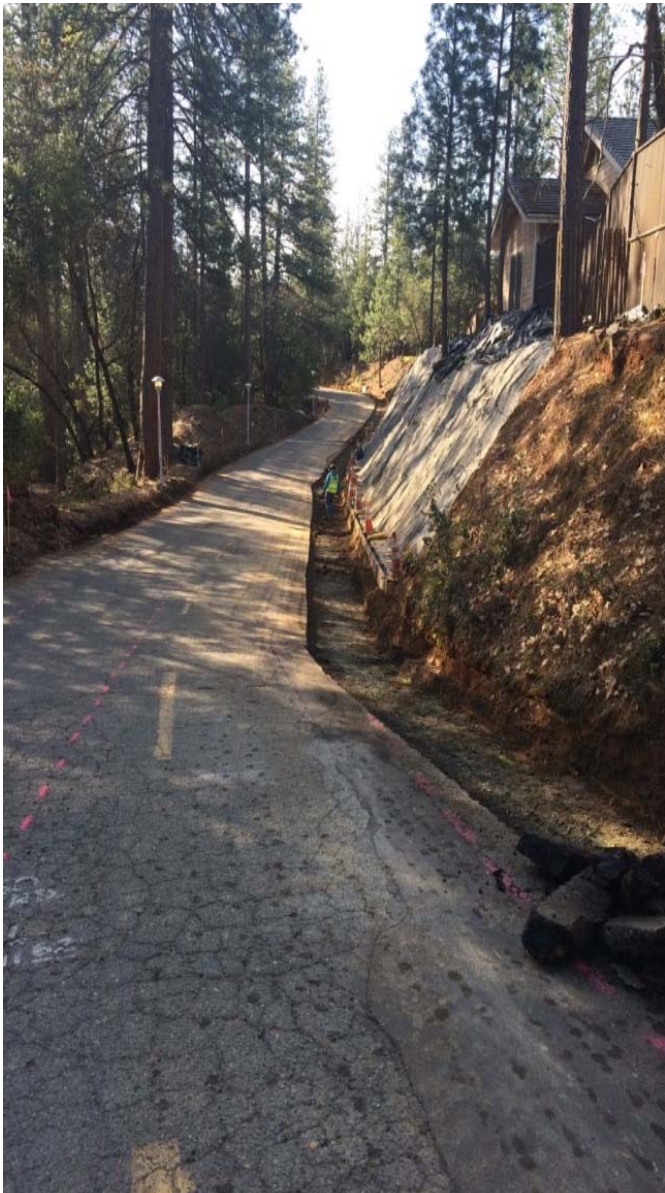

If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 11600 Columbia College Drive Dr., Sonora CA 95370 Tel: 209-575-7927 Email rmartin@kitchell.com

