



Measure E Bond Program COLUMBIA COLLEGE CAMPUS *CONSTRUCTION UPDATE*



UPDATES & ACTIVITIES THAT MAY IMPACT CAMPUS OPERATION

Week of July 8, 2013

MJC NURSING COHORT - REDBUD

Work this week: Mechanical, electrical and plumbing subcontractors are scheduled to finish MEP systems. Also, epoxy landings at exterior doors will be installed along with door trim and door closers.

Access: Limited access through drive isle north of building.
Noise: Moderate noise could occur occasionally.
Parking: Parking impact due to contractor's parking along drive isle.
Dust: Low Impact.
Odors: Low Impact.
Utilities: No impact to utilities is anticipated.



Secondary Data Center

Work this week: This week's work includes continuing installation of mechanical, electrical and plumbing systems and framing interior walls. Outside the building, the GC will continue installing underground utilities.


Access: Section of par course west of building will be closed starting May 21st - July 8th.
Noise: Moderate noise could occur occasionally due to site related activities.
Parking: Moderate impact to parking at tennis courts due to contractor's staging of construction materials.
Dust: Moderate impact due to site related construction activities.
Odors: Low Impact
Utilities: No impact to utilities is anticipated.



Roadways Phase I

Work this week: This week the GC will repair fill slope, fine grade and place AB at Symons Field Rd.

Access: limited access to Oak Pavilion parking lot and no access to Symons Field Rd.
Noise: Moderate noise will occur due to demolition activities.
Parking: Limited Parking at Oak Pavilion parking lot.
Dust: Moderate impact due to site related construction activities.
Odors: Low Impact.
Utilities: No impact to utilities is anticipated.

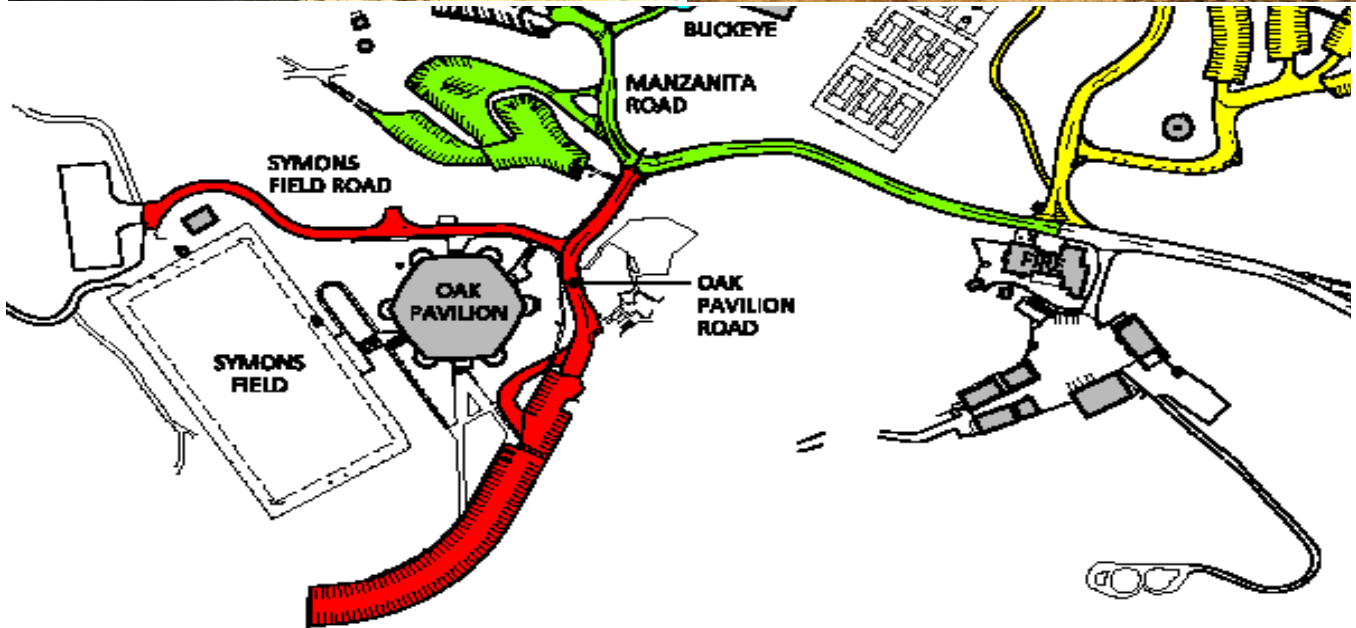

~~~~~  
If there are any questions or concerns contact Kitchell CEM, Measure E Bond Construction Manager, located at 2201 Blue Gum Ave., Modesto CA 95358 Tel: 575-6991 Email [rmartin@kitchell.com](mailto:rmartin@kitchell.com)

