

April 2008

Measure E Bond Program Phase I Projects

PROGRAM PROGRESS

Campus-wide CEQA (CA Environmental Quality Act) compliance documentation was posted for 30-day public review on March 28, 2008.

DESIGN PROGRESS

Public Safety Center: Hazardous material removal is complete. Interim housing is in place and in use. Bidding occurred at the end of March with contract award scheduled for mid-April and construction anticipated to start in mid-May.

Madrone Building: DSA final backcheck review is in process. Bidding is scheduled for April of 2008 with construction anticipated to start at the end of May of 2008.

Science & Natural Resources Center: Schematic Design cost review was complete at the end of March of 2008. Design Development Phase is scheduled to begin in April 2008.

Child Development Center: Construction documents continue to be reviewed by DSA. Final approval is scheduled to be complete by April 2008 with bidding anticipated in May 2008 and construction in June/July 2008.

Calaveras Educational Site: Board has authorized District to begin negotiations.


Oakdale Educational Site: The College and the District continue to review possible sites for a future location.

Scheduled Maintenance Projects – Re-Roof Madrone (Welding) & (Auto): Construction documents have been approved by DSA. Bidding is anticipated for June/July of 2008.


CONSTRUCTION PROGRESS

Buckeye Sewer Pump Replacement: Project closeout phase is now complete.

Science & Natural Resource Center – Schematic Design East Elevation

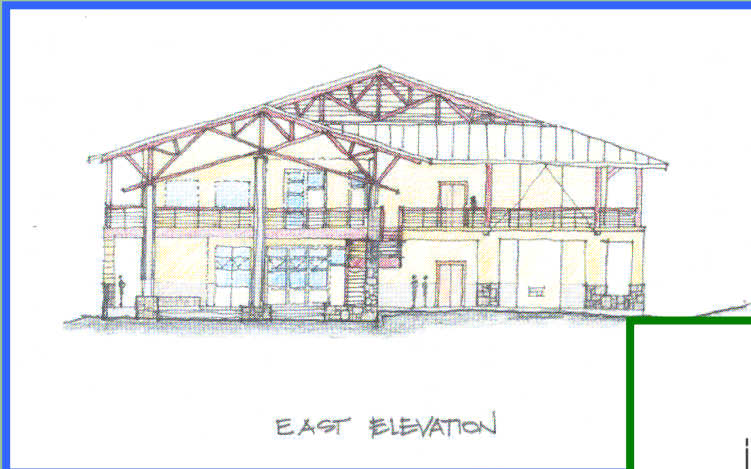

1st Approved Draft Elevation

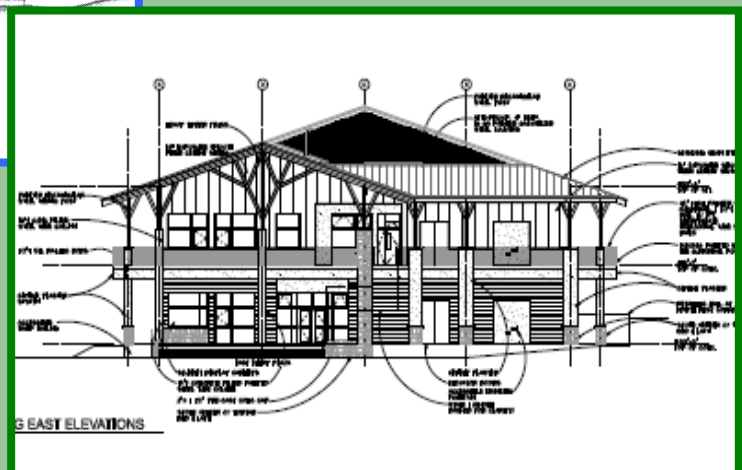

100% Schematic Design

If you have any questions or concerns about ongoing construction activities or would like to get additional information about ongoing design projects, please contact Kitchell, CEM at 575-6991.
