

MJC Measure E Bond Program

Board Update

February 6, 2008

Building High Quality Facilities For

EXCELLENCE IN EDUCATION






Yosemite Community College District





Project Goals





- Provide housing for both men and women

Shelter all fire fighting apparatus









Project Schedule

- PMP shows start of construction August 2008
- Swing Space is nearly complete



- Hazardous Msterial removal to start mid-February
- Construction to begin end of March, 2008, five months ahead of schedule.



Yosemite CCD	2006		2007			2008			2009			2010				2011			2012			2013							
1/24/2008	Q1	Q2	2 Q3	Q4	Q1	Q2 C	Q3 Q4	Q1	Q2	Q3 (Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3 (Q4 Q	1 Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3 Q4
Public Safety Building) (\Diamond								Co	omp	olete	e Ju	ly 20	009									











Project Committee

- Preston Birdwell (CC)
- Gary Mendenhall (CC)
- Greg Elam (CC)
- Joseph Doherty (CC)
- Craig Konklin (Cal Fire)
- Barry Rudolph (Cal Fire)
- Steve Herzog (Cal Fire)
- Jim Toy (Cal Fire)








Campus Master Plan





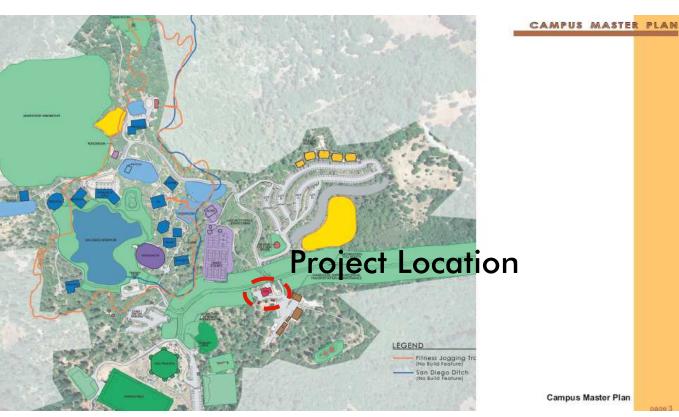












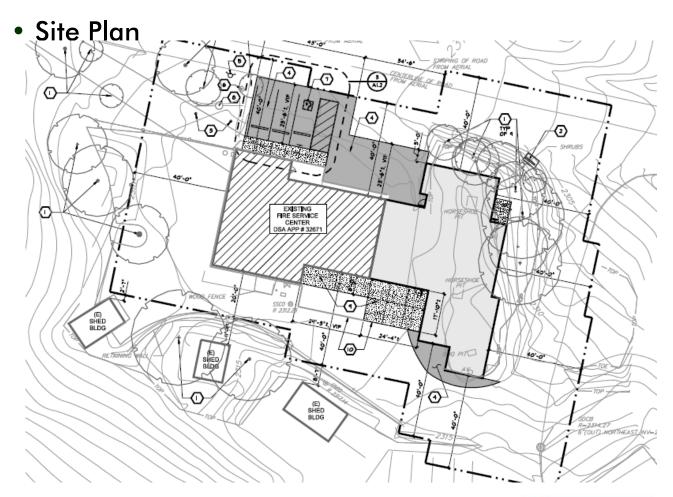












• Floor Plan

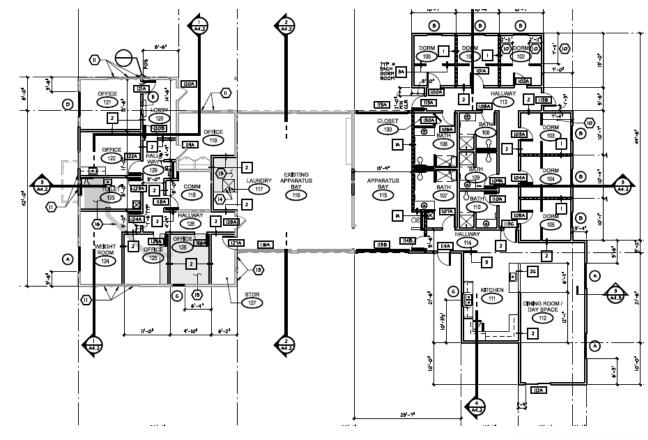





• Rendering













Project will bid for next month



Ground Breaking to be scheduled by the college and district







Question and Answer

January 11, 2008

Building High Quality Facilities For

EXCELLENCE NEDUCATION





Yosemite Community College District
